Estimate No. 014-16-00013
Sanction Dated 17-06-16

M. A. R. 57 (Rule 116)
Measurement Book

No. B 415022

BR 224/12-7-16

Name of Work: Improvements to Medical channel at V.I.Tayalakere layout in

Name of Contractor or nature of Agency: Bajalagutta W.N.14

Date of commencement of work: R. Shivaram, No.4113, Divisional Church Road, Mysuru Rd.

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2					7	8
WORD: EST 00/102/15-16 dt 31.3.2016						
Earth work Excavation by manual means in ordinary soil including all lifts and leads up to 2 mt each and all lifts up to 0.5m from ground level and dumping the excavated soil neatly along the edges of trench and clay Cycle as per Specifications					93.24	7405/-
Add present rate by per 415080 dt 25.5.15			0.79	0.14		
Earth work excavation by mechanical means in ordinary soil including all lifts and leads up to 2 mt each and all lifts up to 0.5m from ground level and dumping the excavated soil neatly along the edges of trench and clay Cycle as per Specifications					265.68	139.40/-
Add present rate by per 415080/2 dt 25.5.15			0.60	0.14		

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Providing and laying in position cement concrete						
		1	50.00	4.50	0.15	33.75	
		1	50.00	4.50	0.15	33.75	
		1	25.00	4.50	0.15	16.87	
						84.37 Cum	136020/-
				@ 1612/- Cum			136004=00
11	Providing and laying in position Cement mortar 1:3 (1 cement : 3 coarse sand) admixture @ 200 ml per 50 kg of cement in cement plaster on rough surface of stone masonry including cleaning and preparing the surface, raking out joints to a depth of 20 mm wherever required, curing etc complete as per specifications and as directed by Engineer-in-charge.						
		1	50.00	4.50	-	225.00	
		1	50.00	4.50	-	225.00	
		1	25.00	4.50	-	112.50	17437/-
			@ 314/- Sq			562.50 Sqm	

M. A. R. 57 (Rule 116)

Measurement Book

No. B 415026

Passed by Cheque for Rs. 1459976=00

Amount admitted for Rs. 1571185=00

by adjustment Rs. 111209=00

Serial No. .....

Name of Work ..... From..... To.....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Executive Engineer, P.W.D. P.H. Basarahalli Division

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
12	Providing and laying 65mm thick Concrete with 1st quality plain blue granite aggregate of specified grading passing through 63mm sieve and retained on 4.75mm sieve in cement concrete proportion 1:2:4 for the floor of Toilet Blocks, Bath Rooms, Kitchen, Verandah, Corridor, Lobby, Staircase, Landing, Ramp, Entrance Porch, Passage, Store Room, Office Room, Class Room, Hall, Dining Room, Bed Room, Drawing Room, Var

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work :- Providing to roads and storm water drain at Tagarekuppe Layout in Begur ward No 14						
	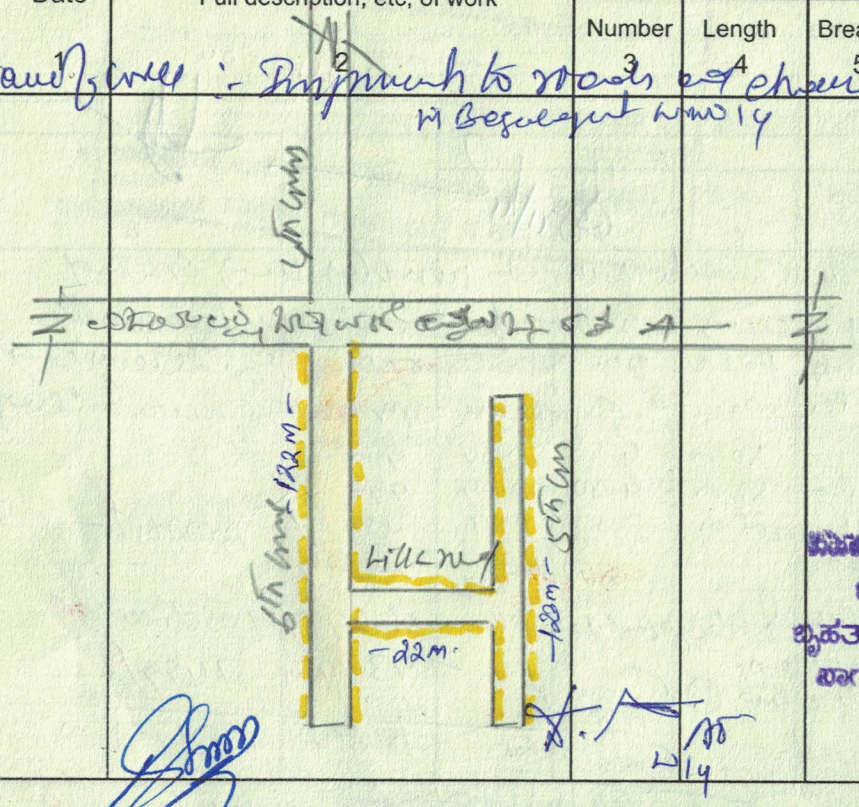						
	ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ಜೆ. ಬಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಶಾಗಲಗುಂಟೆ, ಬೆಂಗಳೂರು - 560 073.						

Serial No. .....
Name of Work .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work
1	2
